11 Jul 2023 • BRA - Bramble Academy



# **Inspection report**

The Bramble Academy Oxclose Lane Mansfield Woodhouse NG19 8DF	Date Of Inspection:05/07/23
Responsible Person: Panayiota Theodosiou	Name Of Inspector(s): Billy Shaw
SENDCo: Maya Dalby	Relevant Contacts: John Wesson (Regional Premises Manager), Danial Wheatley (Site Manager)



# Table of contents

Inspection report	1
Table of contents	2
Introduction	4
Building Details	7
Entrances/Reception	
"Full length glass doors require suffici"	14
Accessible Toilets/Hygiene Rooms	
"Accessible toilet arrangements in the d"	15
<ul><li>"Accessible toilet arrangements in the d"</li></ul>	16
"Accessible toilet is obstructed due to"	17
<ul><li>"Emergency communication pull is not acc"</li></ul>	18
"Accessible toilet signage is unsuitable"	19
"Grab handles and rails in wrong positio"	20
<ul><li>"Emergency communication pull is not acc"</li></ul>	21
"Light switches in accessible toilets sh"	22
<ul><li>"Accessible toilets within the academy r"</li></ul>	23
"Emergency communication pull is not acc"	24
Hallways/Corridors	
"There are several emergency door releas"	25
Stairs/Steps/Ramps/Lifts	
"Edgings of steps/ stairs are damaged/ n"	26
"Hazard tape should be replaced with sui"	27
"Edgings of steps/ stairs are damaged/ n"	28
Classrooms/Communal areas	
■ "Full length glass doors require suffici"	29

11 Jul 2023 • BRA - Bramble Academy



# Table of contents

"Areas of the academy have insufficient"	30
External areas/Playgrounds	
■ "There are a multiple trip hazards prese"	31
Registration drawings	32
Closing Comments	35



## Introduction

#### Introduction

- 1. Improving the physical environment of academies to enable those with disabilities to take better advantage of education, benefits, facilities and services provided
- 2. This Accessibility Plan has been drawn up in consultation with the Greenwood Academies Trust Board, pupils, parents, staff and Advisory Councillors of the Academy and covers the period from June 2021 –June 2024.
- 3. We are committed to providing a fully accessible environment which values and includes all pupils, staff, parents and visitors regardless of their education, physical, sensory, social, spiritual, emotional and cultural needs. We are committed to challenging negative attitudes about disability and accessibility and to developing a culture of awareness, tolerance and inclusion.
- 4. The Greenwood Academies Trust (GAT) plans, over time, to increase the accessibility of provision for all pupils, staff and visitors to all of our sites. Individual Accessibility Plans are produced for each Academy and contain relevant actions to:
- a. Improve access to the physical environment of the Academy, adding specialist facilities as necessary. This covers improvements to the physical environment and physical aids to access education.
- b. Increase access to the curriculum for pupils with a disability, expanding the curriculum as necessary to ensure that pupils with a disability are as equally prepared for life as are the able-bodied pupils. This covers teaching and learning and the wider curriculum of the Academy such as participation in after school clubs, leisure and cultural activities, off site visits etc. It also includes the provision of specialist aids and equipment, which may assist disabled pupils in accessing the curriculum.
- c. Improve the delivery of written information to pupils, staff, parents and visitors with disabilities. This will include hand-outs, timetables, textbooks and information about the Academy and its events. The information will be made available in various preferred formats within a reasonable time frame.
- 5. Attached are Action Plans, relating to these key aspects of accessibility. The plans will be reviewed and adjusted on an annual basis. New Action Plans will be produced every three (3) years.
- 6. We acknowledge that there is a need for on-going awareness raising and training for staff, Trustees and Advisory Councillors in the matter of disability discrimination and the need to inform attitudes on this matter.

11 Jul 2023 • BRA - Bramble Academy



- 7. The Accessibility Plan should be read in conjunction with the relevant sections of following documents:
- a. SEN and Disability Policy
- b. Admissions Policy
- c. Pupil Behaviour and Exclusions Policy
- d. Every Child Matters
- e. Organisation of Pupil Learning
- f. Education Brief
- g. Academy Improvement Plans
- h. Academy Brochures
- i. Asset Management Plan
- 8. The Action Plan for physical accessibility relates to the Access Audit of the Academy, which is undertaken regularly by the Health and Safety Team. It may not be feasible to undertake some of the works during the life of this first Accessibility Plan and therefore some items will roll forward into subsequent plans. The audit will be reviewed prior to the end of each three-year plan period in order to inform the development of the new Plan for the following period.
- 9. As curriculum policies are reviewed, a section relating to access will be added to that on Equality and Diversity. The terms of reference for the GAT Finance and General Purposes (F&GP) and Advisory Council committees will contain an item on 'having regard to matters relating to Access'.
- 10. The Academy Brochure will make reference to this Accessibility Plan.
- 11. The Academy's Complaints Procedure covers the Accessibility Plan.
- 12. Information about our Accessibility Plan will be published in each Academy's Annual Report to Parents (statutory).
- 13. The Plan will be monitored through the Academy Advisory Council. Each Council will produce a termly report on progress against the plan for the GAT F&GP.
- 14. The Academy will work in partnership with all stakeholders in developing and implementing this plan.
- 15. The Plan will be monitored by Ofsted as part of their inspection cycle

11 Jul 2023 • BRA - Bramble Academy



#### Resources

Building Bulletin 102: Designing for disabled children and children with special educational needs.

Building Bulletin 103: Area guidelines for Mainstream Schools

Approved Document M + K

Gov.Uk Fire Safety Risk Assessment- Escape for Disabled People

LABC Building Regulations in Practice - Accessible Toilets by David Spooner

11 Jul 2023 • BRA - Bramble Academy



# **Building Details**

The Bramble Academy

Oxclose Lane

No. of Buildings: 3

No. of Floors: 1

Mansfield Woodhouse

No. of Pupils: 175

No. of Employees: 21

## **Mobility Impairment - Requirements**

#### **Circulation routes**

There is level access from the front and rear of the building.

Car park surface is even with no holes and designated accessible parking spaces.

Joints between surfaces and pavers are not more than 5mm wide.

Inspection chamber covers and service inspection chambers are flush with the surface.

Designated disabled parking spaces are available with drop kerbs and level access to pedestrian walkway.

Communication box at entry to the school grounds is no more than 400mm from ground level

Pedestrian gates or entrances onto the grounds have a min clear opening width of 850mm

Disabled parking space dimensions 4800mm x 2400mm additional hatched extending 1200mm along either side and rear

All disabled parking spaces shall be adequately signed

#### Ramps have;

- o A clear width of 900mm
- o A top and bottom landing
- o An intermediate landing provided between flights and at any change of direction
- o Landings are a minimum of 1200mm long, clear of the swing of any door or gate
- o Kerb/edging min100mm high
- o Handrails set at 900-1000mm height

11 Jul 2023 • BRA - Bramble Academy



#### Communal entrance and reception areas

Doors have a minimum width of 775mm

Threshold is accessible (does not impede wheelchair access)

Means to open the door or doors are automatic

Emergency exit (green button) fitted to the inside

Reception lobby is wide enough to accommodate a wheelchair and companion with a clear manoeuvering space of 1200mm deep x 1800mm wide, if there is a knee recess at least 500mm deep and 1400mm deep and 2200mm wide, if there is no recess.

Any reception desk or counter is designed to accommodate both standing and seated visitors such that at least one section of the counter is a least 1500mm wide with its surface no higher than 760mm and a knee recess, not less than 700mm, above floor level.

#### Dining areas

Access to and from the dining area is suitable width for those with mobility impairment to move around. Furniture is suitable for use for those in a wheelchair and allows interaction between all pupils and staff whilst dining

#### Classrooms

Classrooms with a final exit have a wide door with a ramp for ease of exit in an emergency. Emergency escape from the classroom; ramped egress from final exit

#### Accessible W/Cs

Sufficient accessible toilets for the site. All fixtures and fittings are set at a height suitable for the age range of the intended users

Sufficient manoeuvering space outside the door to the WC

Flush lever is on the open side. A user should be able to flush using a hand, an elbow, or any other part of the body. Some people do it with their chin. If it is not on the open side, it will be impossible to reach from a wheelchair.

Single lever thermostatically controlled tap is located on the corner of the washbasin closest to the toilet.

All facilities e.g. paper towels, soap, toilet paper shall be accessible whilst sitting on the toilet. The ceiling pull switch is located so that it can be operated from the toilet and from an adjacent floor area, the switch has two G pulls, one set at a height between 800 - 1000mm and the other set 100mm above floor level.

11 Jul 2023 • BRA - Bramble Academy



Accessible toilets in primary schools must be age appropriate. The requirements are detailed below:

#### • KS1 (early years - 7)

- o WC with seat height between 300-350mm.
- o Grab rail height to 100-150mm above the seat height and 300-400mm from the centre of the seat,
- o Basin fixed at 500-550mm above floor level.
- o All vertical grab rails at 800mm centres above floor (assuming 600mm grab rail) and at 350-400 centres from the basin.

#### • KS2 (7-11y) and secondary

- o WC with seat height between 420-430mm.
- o Grab rail height to 100-150mm above the seat height and 400-500mm from the centre of the seat
- o Basin fixed at 650-700mm above floor level.
- o All vertical grab rails at 950mm centres above floor (assuming 600mm grab rail) and at 450-500 centres from the basin.

In multi storey buildings there should be an accessible WC on each floor with a travel distance to the nearest such WC being no greater than 25mtrs.

#### Hygiene room

A specialist hygiene room should be available with a fixed/mobile hoist and space for assistants to change a pupil.

In a primary school this should contain a changing bed and accessible WC unless this is included in an adjacent accessible toilet (9m2).

11 Jul 2023 • BRA - Bramble Academy



# Visual Impairment

#### Lighting and contrast

Lighting is suitable and sufficient

Light sources do not create unnecessary shadows (shadows can create optical illusions)

Glare is avoided from shiny or glossy surfaces

Light levels through different rooms and levels are equal

Walls, floors and doorways have sufficient contrast with a difference in light reflectance value (LRV) of >30.

Colour scheme is simple and the number of colours used is limited

Manifestations on glass doors and windows were necessary e.g. full length wider than 400mm

Door frame contrasts against walls and door furniture contrasts with doors.

Sockets and switches contrast to walls.

Signage using braille in raised format is in use.

#### **Circulation routes**

A visually impaired person using a long cane or with an assistance dog needs a walkway measuring at least 1100mm.

A visually impaired person who is being guided needs a width of at least 1200mm.

There is unobstructed height above pedestrian walkways of at least 2300mm (2100mm where a sign is suspended).

Contrasting nosings (with a difference in Light Reflectance Value (LRV)) between the nosing and the body of the step of at least 30) are provided on each step's tread and riser, to help visually impaired people identify the location of the steps, these should be 55mm wide across the whole width on both the

tread and riser. Hatched tape must not be used. Depending on the background a white, black or yellow nosing will usually be appropriate.

A tactile warning surface is incorporated at the top and bottom of external flight of stairs. These textured surfaces are used by the visually impaired to detect when there may be change in level or where pedestrian and vehicular routes may cross.

Handrails are easily distinguishable from the background through the use of good visual contrast and have features to prevent guide dogs from walking under the rails, but with sufficient openings between vertical members to ensure that children and wheelchair users can see, and be seen, through the railings. Handrails should be of a material that is not cold to the touch when temperatures are low.

11 Jul 2023 • BRA - Bramble Academy



Unobstructed height above a pedestrian way is also important, especially for visually impaired people.

This should be a minimum of 2300mm. Where a sign is suspended over a walkway a minimum clearance of 2100mm is acceptable. Where trees overhang a walkway it is advisable to cut them back

to at least 3000mm clear height to allow room for regrowth.

NB people with a visual impairment often lose the ability to distinguish between colours; therefore contrast is important. Contrast can be assessed by taking a photograph of the area e.g. flight of stairs.

accessible WC and printing the photo in monotone. If the edge of the steps, railings fittings etc. can be

clearly distinguished there is sufficient contrast.

#### **Communal lifts**

Tactile indication, to identify each storey, is provided on the landing and adjacent to the call button. Tactile indication to confirm the floor selection is provided on, or adjacent to, the lift buttons within the car.

A raised button within the car indicates the ground floor.

Where the lift serves more than three storeys, it provides visual and audible indicators to identify the floor reached.

## **Hearing Impairment**

Visual alarms such as beacons are mounted at a minimum height of 2.1m from floor level, in a position that is likely to attract attention.

Visual alarms (beacons) are in use in where those with hearing impairment might be alone, such as accessible toilets, where the background noise might exceed 90 dB(A) or where hearing protection is likely to be used for example in music rooms and D&T rooms. For accessible toilets, the alarm must be easily visible by somebody seated on the toilet.

Hearing loops are in place at reception areas with portable hearing loops available to hearing impaired people when required throughout the site. This must be indicated with signage.

11 Jul 2023 • BRA - Bramble Academy



	Pass	Action Required - 1 Month	Action Required - 6 Months	Action Required - Immediate	No status
Carpark/Approach	0	0	0	0	0
	Pass	Action Required - 1 Month	Action Required - 6 Months	Action Required - Immediate	No status
Entrances/Reception	0	1	0	0	0
	Pass	Action Required - 1 Month	Action Required - 6 Months	Action Required - Immediate	No status
Accessible Toilets/Hygiene Rooms	0	2	5	1	2
	Pass	Action Required - 1 Month	Action Required - 6 Months	Action Required - Immediate	No status
Hallways/Corridors	0	0	1	0	0
	Pass	Action Required - 1 Month	Action Required - 6 Months	Action Required - Immediate	No status
Stairs/Steps/Ramps/Lifts	0	3	0	0	0
	Pass	Action Required - 1 Month	Action Required - 6 Months	Action Required - Immediate	No status
Classrooms/Communal areas	0	1	0	0	1
	Pass	Action Required - 1 Month	Action Required - 6 Months	Action Required - Immediate	No status
External areas/Playgrounds	0	0	1	0	0

11 Jul 2023 • BRA - Bramble Academy



	Pass	Action Required - 1 Month	Action Required - 6 Months	Action Required - Immediate	No status
Specific arrangements	0	0	0	0	0
Mobility Impairment	0	0	0	0	0
Visual Impairment	0	0	0	0	0
Hearing Impairment	0	0	0	0	0
Sensory Impairment	0	0	0	0	0

	Pass	Action Required - 1 Month	Action Required - 6 Months	Action Required - Immediate	No status
Curriculum Access	0	0	0	0	0
Mobility Impairment	0	0	0	0	0
Visual Impairment	0	0	0	0	0
Hearing Impairment	0	0	0	0	0
Sensory Impairment	0	0	0	0	0
Room Size/ Requirements	0	0	0	0	0

	Pass	Action Required - 1 Month	Action Required - 6 Months	Action Required - Immediate	No status
Document Check	0	0	0	0	0

11 Jul 2023 • BRA - Bramble Academy




Entrances/Reception

**ACTION REQUIRED - 1 MONTH** 

Full length glass doors require sufficient manifestation markings installing in line with Approved Doc K





Registration drawing

Inspector

Registration time

bramble B1

Billy Shaw

5 Jul 2023, 10:21:40

11 Jul 2023 • BRA - Bramble Academy



Accessible Toilets/Hygiene Rooms


NO STATUS

Accessible toilet arrangements in the dining area may require possible improvements, this would include extensive works to bring the room to the recommended size (2200mmx1500mm) in addition to sufficient grab rails, contrast, etc.

There are however no pupils that require use of an accessible toilet, however consideration must be taken to improving these facilities where possible.

Adaptations or sufficient temporary arrangements will be required in the event of a pupil attending the academy with additional requirements.





Registration drawing

Inspector

Registration time

Bramble B2

Billy Shaw

5 Jul 2023, 11:02:11

11 Jul 2023 • BRA - Bramble Academy



#### Accessible Toilets/Hygiene Rooms


NO STATUS

Accessible toilet arrangements in the dining area may require possible improvements, this would include extensive works to bring the room to the recommended size (2200mmx1500mm) in addition to sufficient grab rails, contrast, etc.

There are however no pupils that require use of an accessible toilet, however consideration must be taken to improving these facilities where possible.

Adaptations or sufficient temporary arrangements will be required in the event of a pupil attending the academy with additional requirements.





Registration drawing

Inspector

Registration time

Bramble B2

Billy Shaw

5 Jul 2023, 11:02:02

11 Jul 2023 • BRA - Bramble Academy




#### Accessible Toilets/Hygiene Rooms

### **ACTION REQUIRED - IMMEDIATE**

Accessible toilet is obstructed due to being used as a storage area.

Clear obstructions and ensure that the accessible toilet is fit for purpose.





Registration drawing

Inspector

Registration time

bramble B1

Billy Shaw

5 Jul 2023, 10:53:14

11 Jul 2023 • BRA - Bramble Academy



#### Accessible Toilets/Hygiene Rooms

### **ACTION REQUIRED - 6 MONTHS**

Emergency communication pull is not accessible.


Emergency communication pull should be within reach of the toilet, with a red triangle positioned at 100mm, and between 800mm - 1000mm from the floor.

No seat installed within shower.

Install seat at 480mm in line with approved doc M

There are currently two rooms containing showers within the academy, it may be determined which of these is the designated hygiene room with works prioritized between the rooms as necessary.





Registration drawing
Inspector

Registration time

bramble B1

Billy Shaw

5 Jul 2023, 10:51:39

11 Jul 2023 • BRA - Bramble Academy




Accessible Toilets/Hygiene Rooms

**ACTION REQUIRED - 1 MONTH** 

Accessible toilet signage is unsuitable and requires replacing with adequate signage.





Registration drawing

Inspector

Registration time

bramble B1

Billy Shaw

5 Jul 2023, 10:45:17

11 Jul 2023 • BRA - Bramble Academy



#### Accessible Toilets/Hygiene Rooms


**ACTION REQUIRED - 6 MONTHS** 

Grab handles and rails in wrong position.

Relocate to correct positions following guidance in Approved Doc M.

Missing grab rail





Registration drawing

Inspector

Registration time

bramble B1

Billy Shaw

5 Jul 2023, 10:44:40

11 Jul 2023 • BRA - Bramble Academy



#### Accessible Toilets/Hygiene Rooms

### **ACTION REQUIRED - 6 MONTHS**


Emergency communication pull is not accessible.


Emergency communication pull should be within reach of the toilet, with a red triangle positioned at 100mm, and between 800mm - 1000mm from the floor.

No seat installed within shower.

Install seat at 480mm in line with approved doc M

There are currently two rooms containing showers within the academy, it may be determined which of these is the designated hygiene room with works prioritized between the rooms as necessary.

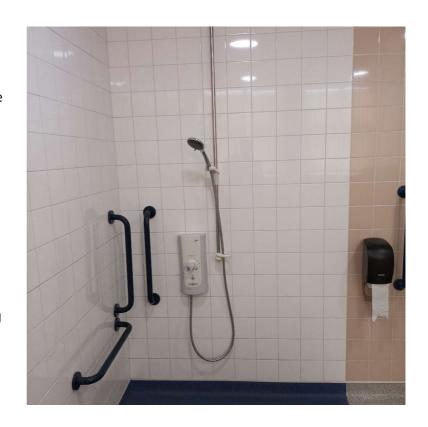



Registration drawing

Inspector

Registration time

bramble B1

Billy Shaw

5 Jul 2023, 10:43:21

11 Jul 2023 • BRA - Bramble Academy




#### Accessible Toilets/Hygiene Rooms

### **ACTION REQUIRED - 6 MONTHS**

Light switches in accessible toilets should be easily operable with a closed fist.

Although there are no persons currently in attendance that require use of an accessible toilet consider changing light switch to a unit more suitable.





Registration drawing

Inspector

Registration time

Bramble B3

Billy Shaw

5 Jul 2023, 10:14:05

11 Jul 2023 • BRA - Bramble Academy




#### Accessible Toilets/Hygiene Rooms

### **ACTION REQUIRED - 6 MONTHS**

Accessible toilets within the academy require visual beacons installing.

All accessible toilets should be checked with replacement beacons installed as necessary.





Registration drawing

Inspector

Registration time

Bramble B3

Billy Shaw

5 Jul 2023, 10:11:17

11 Jul 2023 • BRA - Bramble Academy




#### Accessible Toilets/Hygiene Rooms

**ACTION REQUIRED - 1 MONTH** 

Emergency communication pull is not accessible.

Emergency communication pull should be within reach of the toilet, with a red triangle positioned at 100mm, and between 800mm - 1000mm from the floor.





Registration drawing

Inspector

Registration time

Bramble B3

Billy Shaw

5 Jul 2023, 10:08:38

11 Jul 2023 • BRA - Bramble Academy



#### Hallways/Corridors


### **ACTION REQUIRED - 6 MONTHS**

There are several emergency door release controls ore positioned too high.

Emergency door release controls should be positioned between 800mm-1200mm from ground level to allow ease of access.

All control units within the academy should be checked and repositioned where necessary.





Registration drawing

Inspector

Registration time

Bramble B3

Billy Shaw

5 Jul 2023, 10:16:39

11 Jul 2023 • BRA - Bramble Academy




Stairs/Steps/Ramps/Lifts

**ACTION REQUIRED - 1 MONTH** 

Edgings of steps/ stairs are damaged/ not marked.

Mark edges of steps/stairs with a slip resistant and contrasting nosing extending along the full width of the step to a depth of 50mm on tread and riser.





Registration drawing

Inspector

Registration time

Bramble B2

Billy Shaw

5 Jul 2023, 10:57:15

11 Jul 2023 • BRA - Bramble Academy





Stairs/Steps/Ramps/Lifts

**ACTION REQUIRED - 1 MONTH** 

Hazard tape should be replaced with suitable edgings.

Mark edges of steps/stairs with a slip resistant and contrasting nosing extending along the full width of the step to a depth of 50mm on tread and riser.

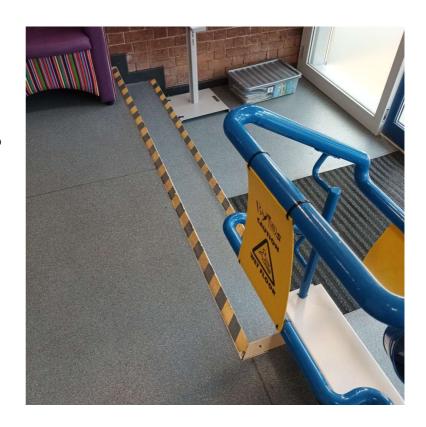



Registration drawing

Inspector

Registration time

bramble B1

Billy Shaw

5 Jul 2023, 10:22:21

11 Jul 2023 • BRA - Bramble Academy




Stairs/Steps/Ramps/Lifts

**ACTION REQUIRED - 1 MONTH** 

Edgings of steps/ stairs are damaged/ not marked.

Mark edges of steps/stairs with a slip resistant and contrasting nosing extending along the full width of the step to a depth of 50mm on tread and riser.





Registration drawing

Inspector

Registration time

Bramble B3

Billy Shaw

5 Jul 2023, 10:18:06

11 Jul 2023 • BRA - Bramble Academy




Classrooms/Communal areas

**ACTION REQUIRED - 1 MONTH** 

Full length glass doors require sufficient manifestation markings installing in line with Approved Doc K





Registration drawing

Inspector

Registration time

bramble B1

Billy Shaw

5 Jul 2023, 10:49:10

11 Jul 2023 • BRA - Bramble Academy



Classrooms/Communal areas


NO STATUS

Areas of the academy have insufficient levels of contrast.

This issue will be progressively resolved throughout the Trust during periods of redecoration works.

Where any pupils are present with visual impairments, temporary arrangements should be implemented where necessary.





Registration drawing

Inspector

Registration time

bramble B1

Billy Shaw

5 Jul 2023, 10:36:15

11 Jul 2023 • BRA - Bramble Academy



### External areas/Playgrounds

**ACTION REQUIRED - 6 MONTHS** 

There are a multiple trip hazards present within this area of the playground.

The area is due for refurbishment throughout the summer period.





Registration drawing

Inspector

Registration time

bramble B1

Billy Shaw

5 Jul 2023, 11:10:46

11 Jul 2023 • BRA - Bramble Academy








#### bramble B1

- 14 Entrances/Reception
- 17 Accessible Toilets/Hygiene Rooms
- 18 Accessible Toilets/Hygiene Rooms
- 19 Accessible Toilets/Hygiene Rooms
- 20 Accessible Toilets/Hygiene Rooms21 Accessible Toilets/Hygiene Rooms
- 27 Chaire (Chara /Daves // ift-
- 27 Stairs/Steps/Ramps/Lifts
- 29 Classrooms/Communal areas
- 30 Classrooms/Communal areas
- 31 External areas/Playgrounds



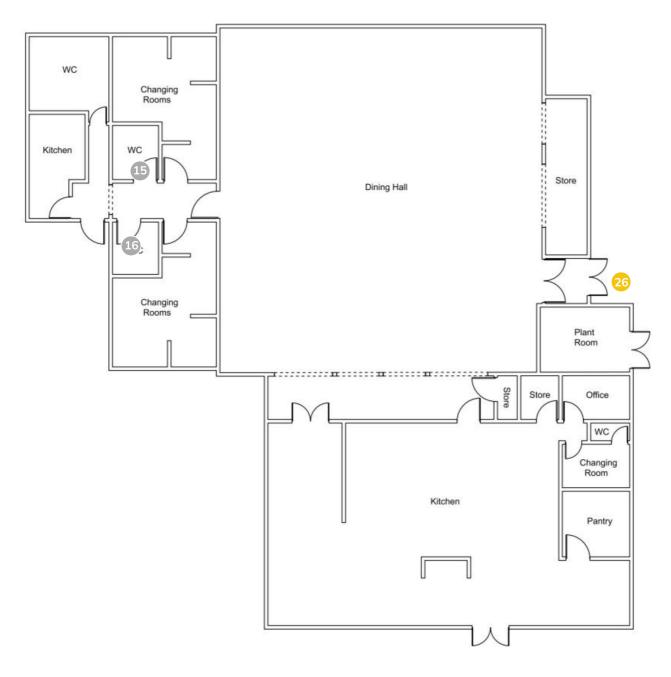

#### **Bramble B2**

15 Accessible Toilets/Hygiene Rooms

16 Accessible Toilets/Hygiene Rooms

26 Stairs/Steps/Ramps/Lifts





#### **Bramble B3**

- 22 Accessible Toilets/Hygiene Rooms
- 23 Accessible Toilets/Hygiene Rooms
- 24 Accessible Toilets/Hygiene Rooms
- 25 Hallways/Corridors
- 28 Stairs/Steps/Ramps/Lifts

11 Jul 2023 • BRA - Bramble Academy



# **Closing Comments**

Name Of Inspector(s)Billy Shaw	Signature	11 Jul 2023, 13:50:18 Time
Date of Inspection:05/07/23	Date of Review: 5.7.26	
